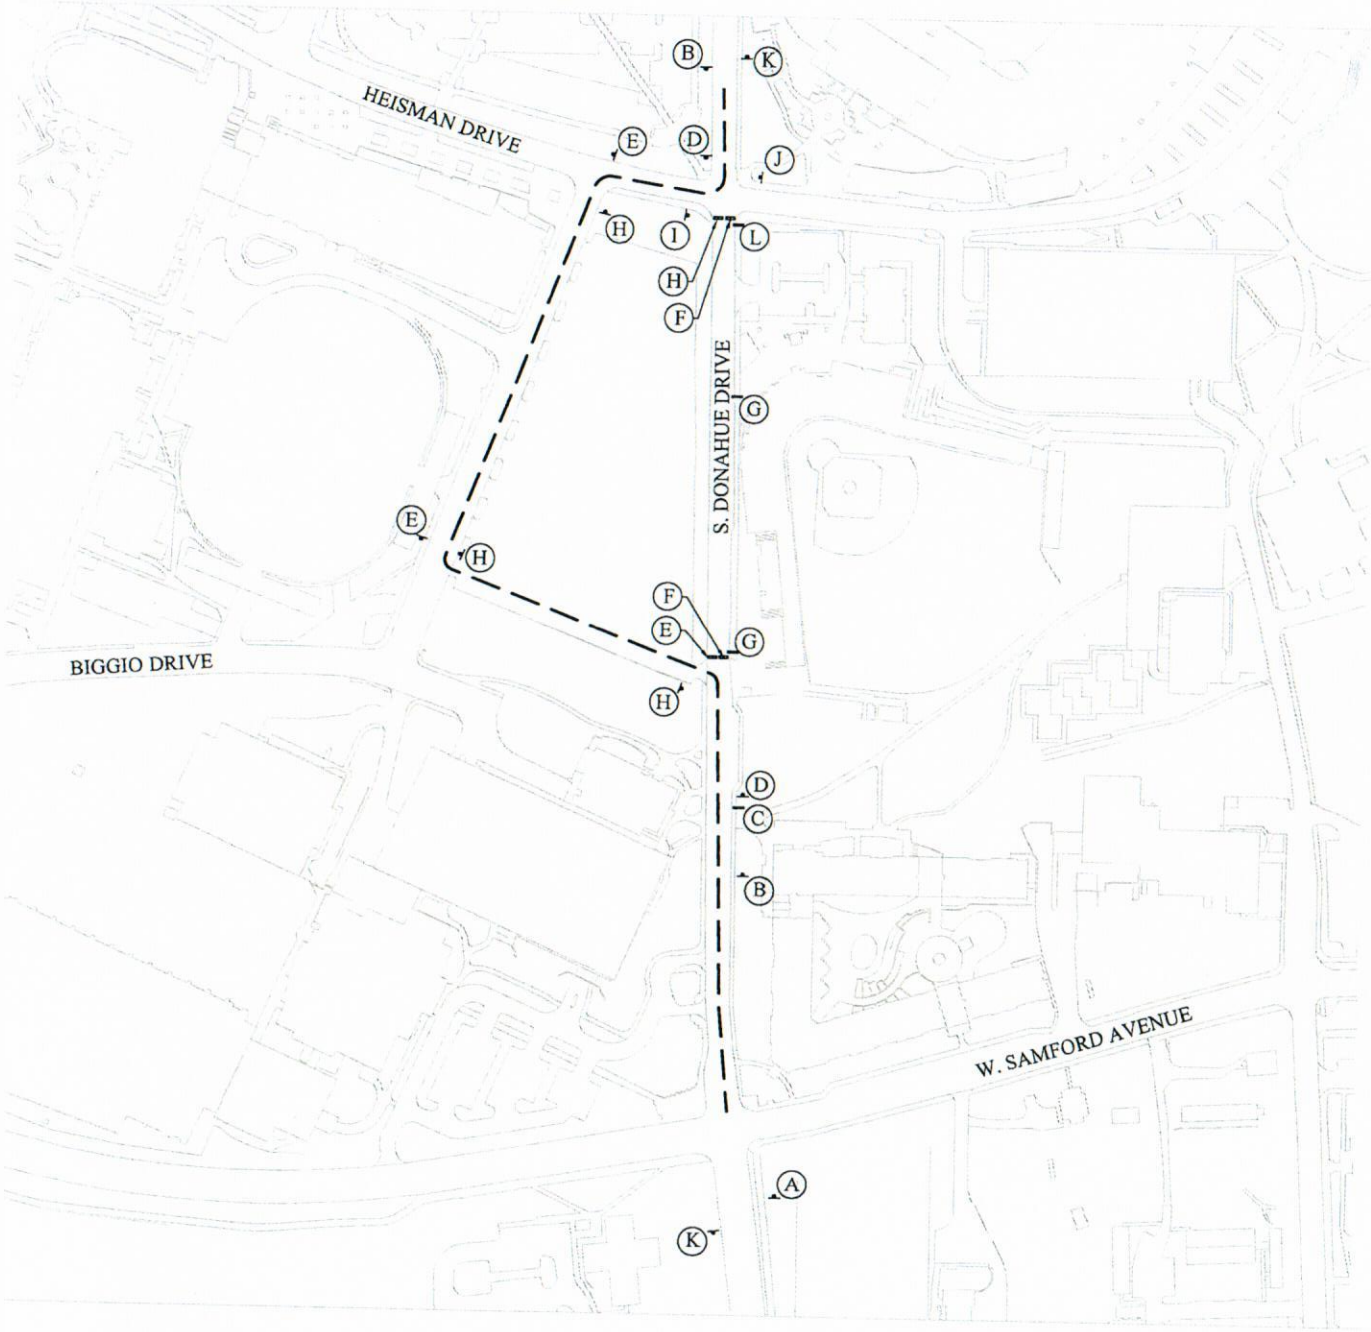


## TRAFFIC CONTROL LEGEND

- TYPE III BARRICADE
- A-FRAME FOLDING BARRICADE
- POST MOUNTED SIGN
- (A) ROAD WORK AHEAD (W20-1) 36"x36"
- (B) ROAD CLOSED AHEAD (W20-2) 36"x36"
- (C) SIDEWALK CLOSED AHEAD LEFT ARROW CROSS HERE (R9-11L) (24"X18")
- (D) DETOUR AHEAD (W20-1) 36"x36"
- (E) DETOUR LEFT ARROW (M4-10L) 48"X18"
- (F) ROAD CLOSED (R11-2) (48" x 30")
- (G) SIDEWALK CLOSED (R9-9) (24"x12")
- (H) DETOUR RIGHT ARROW (M4-10R) 48"x18"
- (I) NO RIGHT TURN (R3-1) 30"x30"
- (J) NO LEFT TURN (R3-2) 36"x36"
- (K) END DETOUR (M4-9A) 36"x24"
- (L) SIDEWALK CLOSED AHEAD RIGHT ARROW CROSS HERE (R9-11L) (24"X18")

NOTES

1. CONTRACTOR TO HAVE WRITTEN APPROVAL FROM AUBURN UNIVERSITY PRIOR TO IMPLEMENTING ANY ROAD CLOSURES. THIS PLAN IS INTENDED TO BE UTILIZED IN LOW TRAFFIC AND PEDESTRIAN VOLUME CONDITIONS.
2. TYPE III BARRICADES TO INCLUDE AT A MINIMUM ONE SOLAR POWERED FLASHING BEACON PER BARRICADE. SIGNS TO BE ATTACHED TO BARRICADE AS INDICATED IN THE PLAN AND TRAFFIC CONTROL LEGEND.
3. PEDESTRIAN CLOSURE SIGNS TO BE AFFIXED TO A TRADITIONAL A FRAME FOLDING BARRICADE AND IMPLEMENTED ONLY WHEN WORK IS COMMENCING. PEDESTRIAN BARRICADES AND SIGNAGE SHALL BE REMOVED AT THE END OF THE DAY OR WHEN WORK IS NOT REQUIRING A SIDEWALK CLOSURE.
4. THIS TRAFFIC CONTROL PLAN DOES NOT ALLEVIATE ANY SAFETY RESPONSIBILITY FROM THE CONTRACTOR. IT IS INCUMBENT UPON THE CONTRACTOR TO ENSURE PEDESTRIAN TRAFFIC AND FLOW DOES NOT CHOKE NEAR ANY WORK BEING PERFORMED.
5. ALL SIGNAGE TO COMPLY WITH THE LATEST EDITION OF THE MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES (MUTCD).
6. DETOUR SIGNAGE SHALL BE INSTALLED PRIOR TO ROAD CLOSURE AND BAGGED PRIOR TO EXECUTING THE APPROVED CLOSURE. ONCE WORK IS COMPLETED, SIGNAGE SHALL BE REMOVED IMMEDIATELY.

GRAPHIC SCALE

( IN FEET )
1 inch = 50 ft.

AUBURN UNIVERSITY
Facilities Management
1161 West Samford Avenue
Auburn University, AL 36849
Phone: (334) 844-9450
Fax: (334) 844-9458
*Safety is our first priority. Think Safety; Act Safely.*

ALABAMA LICENSED No. 31938 PROFESSIONAL ENGINEER

PLAINSMAN PARK
LED LIGHTING UPGRADE REPLACEMENT
AUBURN, AL

| | |
|---|---|
| SHEET TITLE: | TRAFFIC CONTROL PLAN |
| DRAWN BY: | B. BURMESTER |
| CHECKED BY: | W. PEACOCK |
| DATE: | 12/8/16 |
| FILE NUMBER: | – |
| PROJECT NUMBER: | 16–237 |
| SHEET NUMBER: | TCP1.R0 |
